

**Program Manager's Report**  
**Construction Activity...**  
**April 2008**

# **CONSTRUCTION STATUS**

**Construction Complete and Acceptance  
Complete and on this Evening's Agenda  
PROJECT 10 A**

# **CONSTRUCTION STATUS**

## **Project 6A-1**

- **Contractor installed 854 feet of 16-inch line**
- **Contractor is working on tunnels in advance of large inch pipe delivery**
- **Large inch pipe delivery scheduled to begin this month**

# **CONSTRUCTION STATUS**

## **Project 10B**

- **Contractor completed the tunnel under Cypress Creek and has begun installation of the pipe in the tunnel**
- **Contractor has to date installed a total of approximately 5,472 feet of 42-inch water line**

# **CONSTRUCTION STATUS**

## **Project 15A**

- **Contractor installed an additional 1,823 feet of 36-inch water line bringing the total footage installed to 9,565 feet**
- **Contractor completed installation of the primary liner for the 36-inch water line**

# **CONSTRUCTION STATUS**

## **Project 17-1**


- **Contractor has mobilized and began digging the shafts for the I-45 crossing and the Greens Bayou crossing**
- **Delivery of the pipe is expected to begin in April**

# Pipe installed

An additional 2,677 feet of pipe was installed during the reporting period bringing the total footage of water line installed to 180,026 feet, approximately 34.1 miles

# BIDS RECEIVED AND AWARD RECOMMENDED

## Project 7C-3

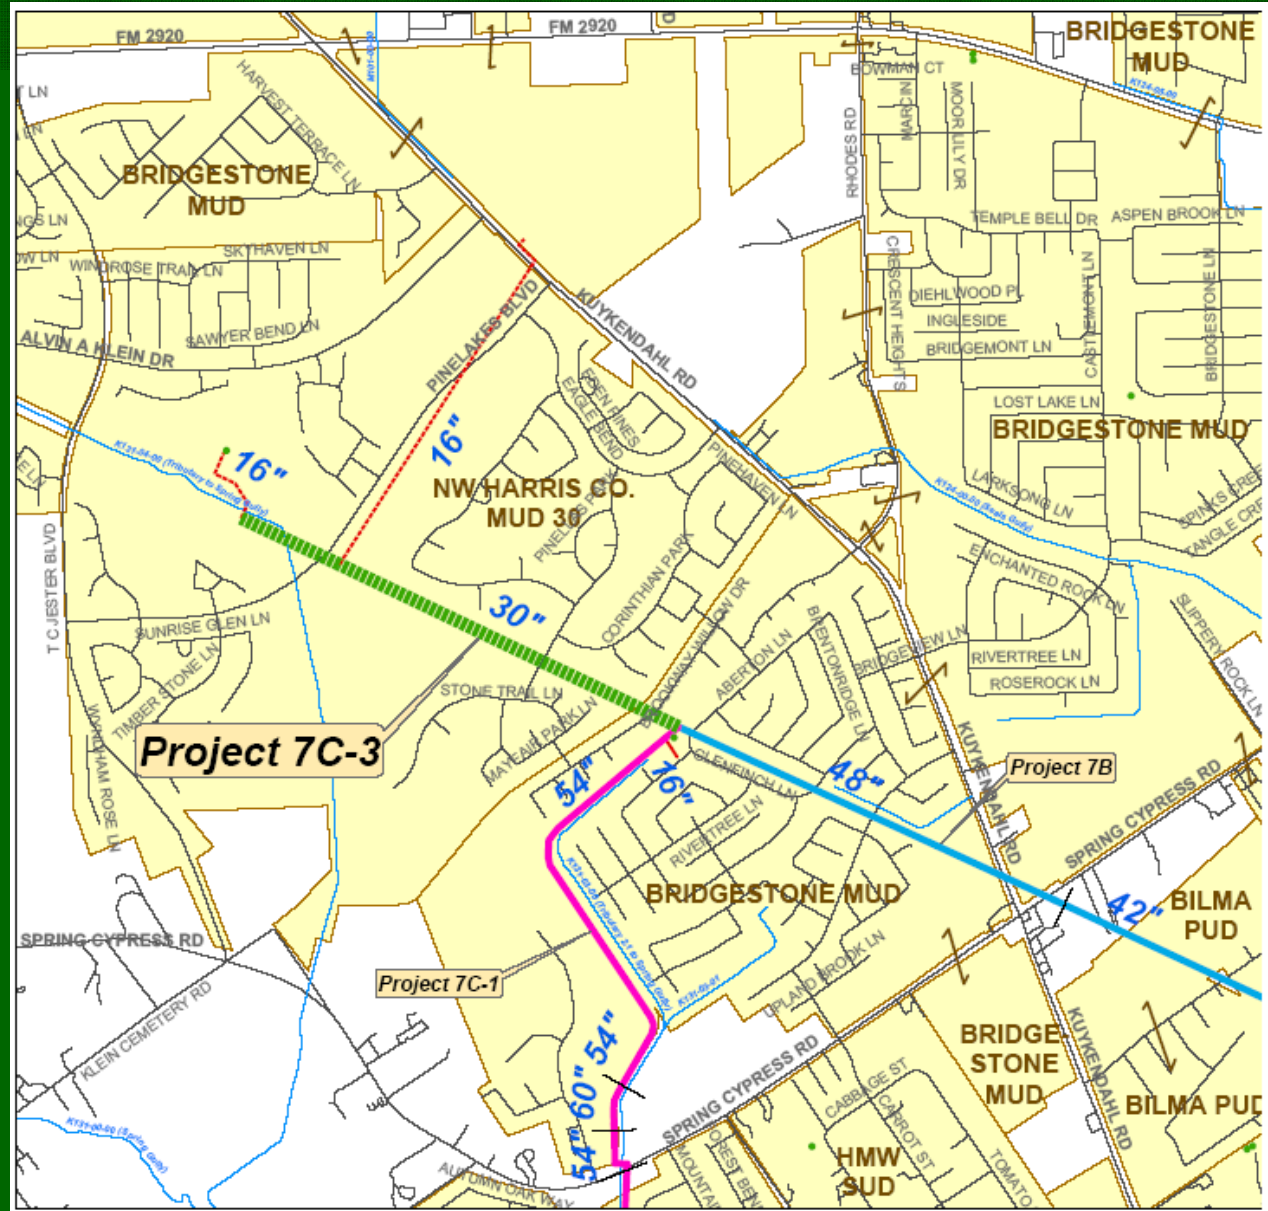


## **BIDS RECEIVED AND AWARD RECOMMENDED**

### **Project 7C-3**

- **March 18, 2008 received and opened 11 bids ranging from \$2,694,822.03 to \$3,782,536.00**
- **TRCU, Ltd. submitted the low bid of \$2,694,822.03**
- **Tabulated bids/reviewed qualification statement and experience information submitted by low bidder.**
- **Recommended to the General Manager that TRCU, Ltd. be awarded the construction contract**
- **Project consists of the installation of approximately 4,800 feet of 30-inch water line and the connection to Northwest HCMUD No. 30 water plant**
- **Substantial completion of the project is specified in 240 calendar days**

# BIDS RECEIVED AND AWARD RECOMMENDED

## Project 16

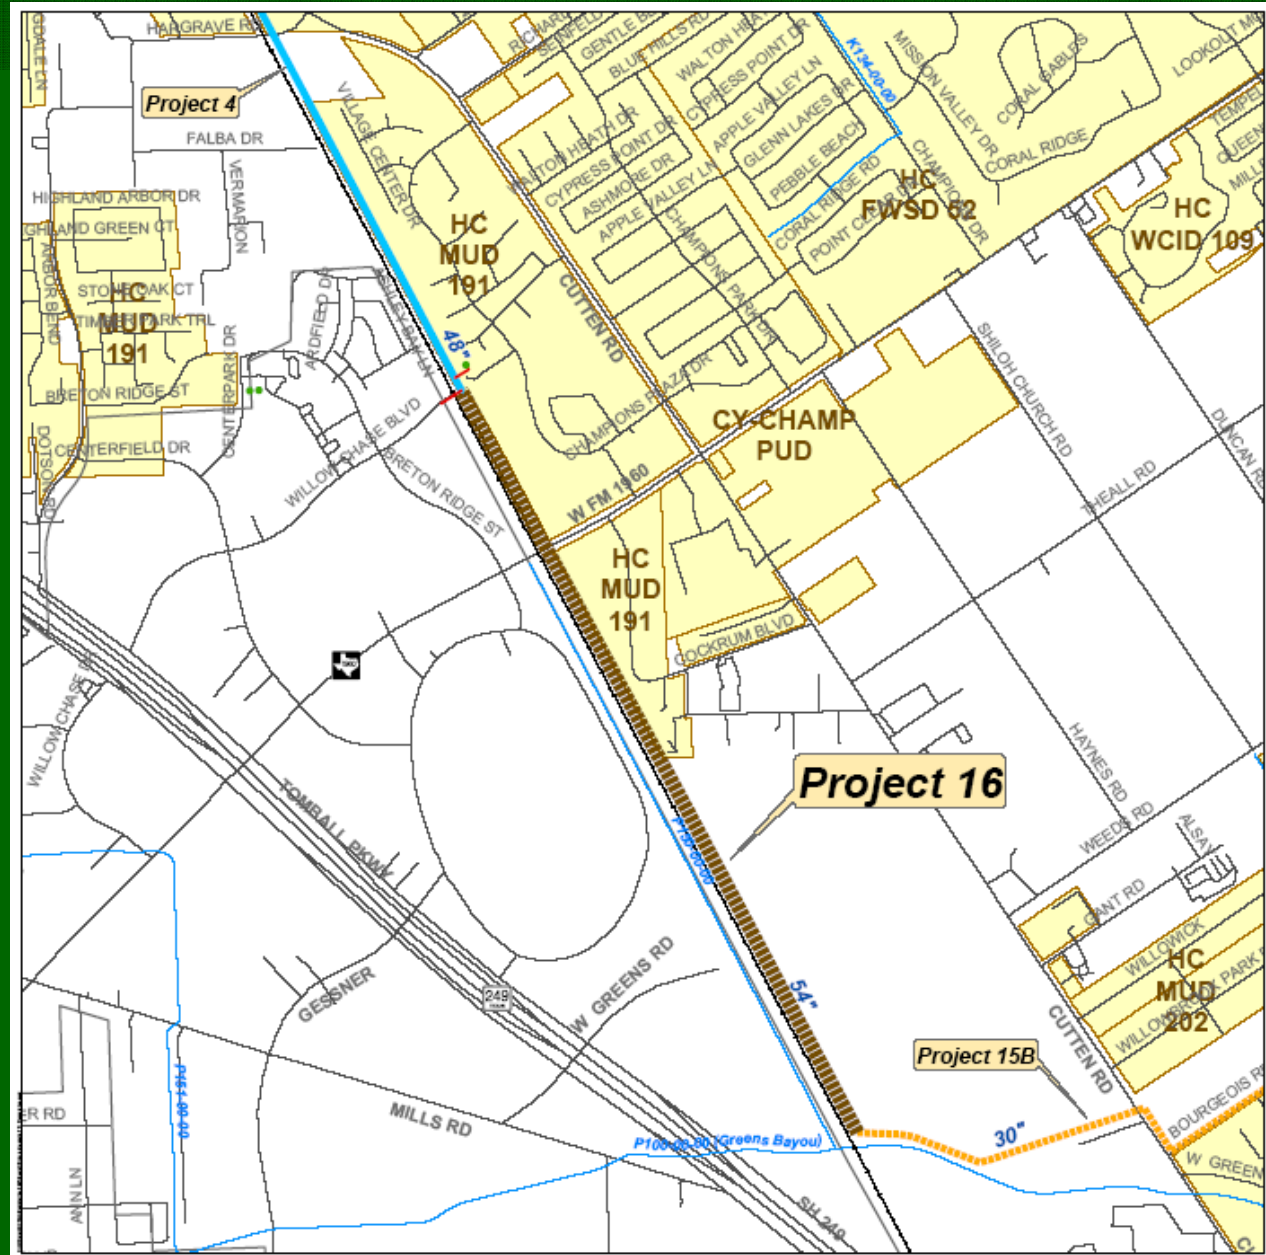

# **BIDS RECEIVED AND AWARD RECOMMENDED**

## **Project 16**

- **March 25, 2008 received and opened 10 bids ranging from \$4,213,126.00 to \$5,414,845.17**
- **Pace Services, L.P. submitted the low bid of \$4,213,126.00**
- **The second low bid of \$4,298,039.50 submitted by Calco Contracting, LTD. was \$84,913.50 more than low bid**
- **Tabulated bids/reviewed qualification statements and experience information submitted by the two lowest bidders.**
- **Based on that review, recommended to the General Manager that Calco Contracting, LTD. be awarded the construction contract**
- **Project primarily consists of the installation of approximately 8,000 feet of 54-inch water line**
- **Substantial completion of the project is specified in 330 calendar days**

# **GROUNDWATER TRANSFER PROGRAM**

- **Provided administrative oversight of the GTP systems**
- **Systems continue to be reliable, responsive and function effectively**
- **Provided approximately 2.00 MGD of water to the Buyer Districts during the period**

## **MAJOR ACTIVITIES**

- **Assisting the Authority in its efforts concerning the “Luce Bayou Project”**
- **Continued oversight of engineering efforts on 15 projects**
- **Advertised for bid Project 17, Segment 2**
- **Provided construction administration and project representatives on Projects 6A-1, 10A , 10B, 15A and 17, Segment 1 and construction administration on Projects 4C, 7C-3, 16 and 17, Segment 2**

## **MAJOR ACTIVITIES (continued)**

- **Supported and facilitated the acquisition of easements for Authority projects**
- **Provided oversight of Severn Trent Environmental Services, Inc. activities and their contract to operate the Authority's GTP**
- **Continued efforts aimed at expanding the GTP**
- **Initiated preparation of annual report and application for renewal of the Authority's Harris County Master Storm Water Quality Permit**
